PROJECT RISK MANAGEMENT · GROUP STUDY CASE

Risk Assessment Matrix

Omnichannel Retail Launch 2026

Prepared by Group 3 – Project Management Team · Review date: 3 October 2026 · Planned launch: 10 October 2026

Project context

A local retailer is launching an omnichannel experience that lets customers check real-time stock, buy through a mobile app, pay digitally, and collect orders in store. With the project **80% complete** and launch one week away, the team identified and assessed **25 risks** across IT, store operations, finance, marketing, customer service, and stakeholder management. Each risk is scored as **Likelihood × Impact** (1–5 each) and assigned an owner, a mitigation plan, and a target date.

Risk profile at a glance


25	6	9	10	0
TOTAL RISKS	CRITICAL	HIGH	MEDIUM	LOW

Critical risks requiring immediate action

ID	Critical risk	Score	Owner	Due
R-01	Payment failures at launch	**20**	IT Lead	8 Oct
R-08	No SOP for online transaction complaints	**20**	Customer Service Lead	7 Oct
R-02	App stock does not match in-store stock	**16**	IT Lead	8 Oct
R-04	Defects missed due to incomplete testing	**16**	QA Lead	8 Oct
R-05	Pickup areas and store staff not ready	**16**	Store Operations Lead	8 Oct
R-09	App slowdown or outage under high traffic	**15**	IT Infrastructure Lead	8 Oct

Risk heat map

Risk IDs plotted by likelihood and impact score.

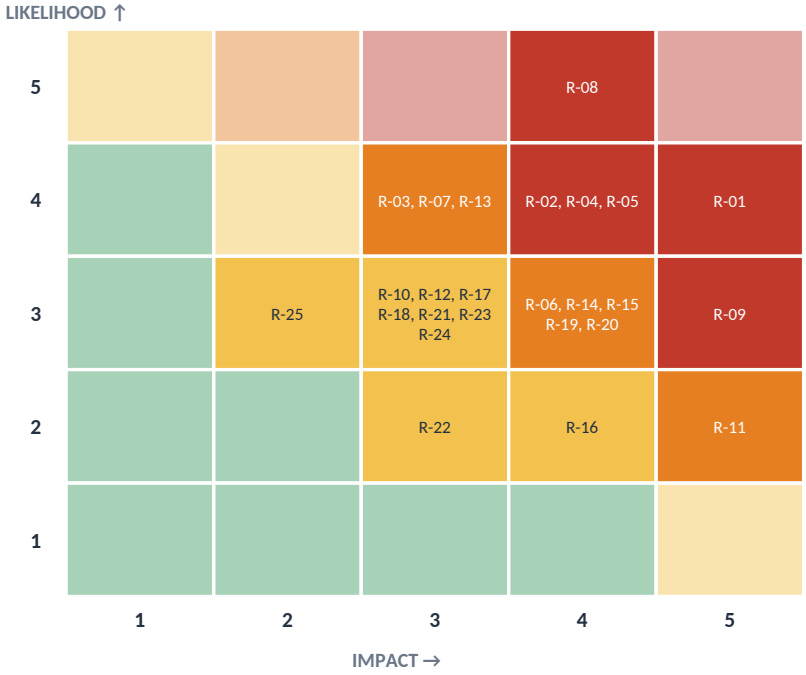

Critical	Score 15–25 · immediate action
High	Score 10–14 · prioritized response
Medium	Score 5–9 · prepare response
Low	Score 1–4 · monitor

Risk register overview — ranked by score

All 25 risks sorted from highest to lowest score. Full analysis for each risk follows in the detailed register.

ID	Risk title	Business area	Category	L	I	Score	Level	Action owner	Target date	Status
R-01	Payment failures at launch	IT	IT	4	5	20	Critical	IT Lead	8 Oct 2026	Open
R-08	No SOP for online transaction complaints	Customer Service	Operational	5	4	20	Critical	Customer Service Lead	7 Oct 2026	Open
R-02	App stock does not match in-store stock	IT / Store Operations	IT	4	4	16	Critical	IT Lead	8 Oct 2026	Open
R-04	Defects missed due to incomplete testing	IT / QA	IT	4	4	16	Critical	QA Lead	8 Oct 2026	Open
R-05	Pickup areas and store staff not ready	Store Operations	Operational	4	4	16	Critical	Store Operations Lead	8 Oct 2026	Open
R-09	App slowdown or outage under high traffic	IT	IT	3	5	15	Critical	IT Infrastructure Lead	8 Oct 2026	Open
R-03	Confusing checkout flow	IT / Product	IT	4	3	12	High	UX Designer	7 Oct 2026	Open
R-06	Logistics vendor delays or cost increase	Procurement / Logistics	Financial	3	4	12	High	Procurement Lead	6 Oct 2026	Open
R-07	Campaign overpromises on service readiness	Marketing	Reputational	4	3	12	High	Marketing Lead	7 Oct 2026	Open
R-13	Additional costs exceed the budget	Finance / PMO	Financial	4	3	12	High	Project Manager	6 Oct 2026	Open
R-14	Stakeholder misalignment on launch scope	PMO / Stakeholders	Strategic	3	4	12	High	Project Manager	6 Oct 2026	Open
R-15	Late feature requests before launch	PMO	Strategic	3	4	12	High	Project Manager	7 Oct 2026	Open
R-19	Slow vendor response to payment errors	IT / Vendor	IT	3	4	12	High	IT Lead	6 Oct 2026	Open
R-20	No service owner after project closure	Operations / Business Owner	Strategic	3	4	12	High	Project Manager	24 Oct 2026	Open
R-11	Customer personal data breach	IT / Legal	Compliance	2	5	10	High	IT Security Lead	9 Oct 2026	Open
R-10	Order status notifications not delivered	IT	IT	3	3	9	Medium	QA Lead	8 Oct 2026	Open
R-12	Payment data mismatch across systems	Finance	Financial	3	3	9	Medium	Finance Controller	9 Oct 2026	Open
R-17	Unclear in-store returns for online orders	Store Operations	Operational	3	3	9	Medium	Store Operations Lead	8 Oct 2026	Open
R-18	Store devices not ready for pickup process	Store Operations / IT	Operational	3	3	9	Medium	Store Operations Lead	8 Oct 2026	Open
R-21	Stores overwhelmed by launch orders	Store Operations	Operational	3	3	9	Medium	Store Operations Lead	9 Oct 2026	Open
R-23	App errors on certain phone models	IT / QA	IT	3	3	9	Medium	QA Lead	8 Oct 2026	Open
R-24	Low customer adoption of the app	Marketing / Business Owner	Strategic	3	3	9	Medium	Marketing Lead	24 Oct 2026	Monitoring
R-16	Key team members unavailable	IT	Operational	2	4	8	Medium	IT Lead	7 Oct 2026	Open
R-22	Unclear or non-compliant promotion terms	Marketing / Legal	Compliance	2	3	6	Medium	Marketing Lead	7 Oct 2026	Open
R-25	Phased launch details not reaching all stores	Store Operations	Operational	3	2	6	Medium	Store Operations Lead	9 Oct 2026	Open

Detailed risk register

Risk statements follow the format: *Because [cause], there is a risk of [event], which may cause [impact].*

Risk	Risk description	Root cause	Business consequences	Existing controls	Mitigation actions
R-01 **Payment failures at launch** IT · IT CRITICAL · 20	Because the payment system still fails on some transactions and testing is incomplete, there is a risk of failed transactions or duplicate charges at launch, which may cause customers to abandon purchases and increase complaints.	Payment gateway integration was completed close to the deadline; payment flow testing is incomplete.	Lost sales, refunds and chargebacks, and reduced customer trust on day one.	Daily error log monitoring. Needs Improvement	Fix the errors and retest all payment methods; temporarily disable any method that still fails; prepare a fallback option (order online, pay in store). **Owner:** IT Lead · **Due:** 8 Oct · **Status:** Open
R-02 **App stock does not match in-store stock** IT / Store Operations · IT CRITICAL · 16	Because the inventory dashboard is not fully synchronized with store stock, there is a risk that customers purchase items that are actually out of stock (overselling), which may lead to cancelled orders and dissatisfied customers.	Store-to-app stock data integration is incomplete; stock updates are not yet real-time.	Order cancellations, refunds, complaints, and damage to the online service's reputation.	Manual stock checks by store staff. Needs Improvement	Display only products with verified stock data; reserve buffer stock for online orders; reconcile app and store stock daily. **Owner:** IT Lead · **Due:** 8 Oct · **Status:** Open
R-03 **Confusing checkout flow** IT / Product · IT HIGH · 12	Because several checkout steps remain confusing, there is a risk that customers abandon the purchase midway, which may cause online sales to fall below target.	The checkout flow has not been tested with real users.	Low online sales; more questions and complaints directed to Customer Service.	None in place. Ineffective	Run a quick usability test with 5–8 users; fix the 3–5 most confusing steps; add brief in-app guidance. **Owner:** UX Designer · **Due:** 7 Oct · **Status:** Open
R-04 **Defects missed due to incomplete testing** IT / QA · IT CRITICAL · 16	Because testing is only 60% complete, there is a risk that undetected defects appear once customers use the app, which may disrupt the service after launch.	Testing time was compressed by development delays.	Post-launch emergency fixes are more costly; customer dissatisfaction; negative reviews.	Manual testing by the QA team. Needs Improvement	Prioritize testing of the core journey (product search, payment, pickup); freeze new features before launch; keep a support team on standby for 2 weeks after launch. **Owner:** QA Lead · **Due:** 8 Oct · **Status:** Open
R-05 **Pickup areas and store staff not ready** Store Operations · Operational CRITICAL · 16	Because pickup area renovation is unfinished and not all staff have completed training, there is a risk that in-store pickup is slow and disorganized, which may cause long queues and complaints.	Renovation and training schedules are too close to the launch date.	Poor first impression for customers; weakened perception of the click-and-collect service.	No store readiness checklist in place. Ineffective	Offer in-store pickup only at pilot stores that pass the readiness check; provide rapid training and a quick-reference guide for staff. **Owner:** Store Operations Lead · **Due:** 8 Oct · **Status:** Open
R-06 **Logistics vendor delays or cost increase** Procurement / Logistics · Financial HIGH · 12	Because the logistics vendor has requested additional fees to guarantee on-time delivery, there is a risk of exceeding the budget, or of late deliveries if the request is declined, which may cause orders to reach customers late.	The original contract does not include a clear delivery time guarantee (SLA).	Budget overrun or late delivery to customers.	Standard vendor contract. Needs Improvement	Approve additional fees only with a written on-time guarantee and late-delivery penalties; prepare a backup vendor; limit the delivery area in the initial phase. **Owner:** Procurement Lead · **Due:** 6 Oct · **Status:** Open
R-07 **Campaign overpromises on service readiness** Marketing · Reputational HIGH · 12	Because campaign materials have already been published promising a full service, there is a risk that the services available at launch fall short of customer expectations, which may cause disappointment and negative social media comments.	The campaign was created before operational readiness was confirmed.	Damage to brand reputation; increased complaints.	None in place. Ineffective	Revise the campaign message to state that in-store pickup will be rolled out gradually at selected stores, and publish the list of participating stores. **Owner:** Marketing Lead · **Due:** 7 Oct · **Status:** Open

Risk	Risk description	Root cause	Business consequences	Existing controls	Mitigation actions
R-08 **No SOP for online transaction complaints** Customer Service · Operational **CRITICAL · 20**	Because the Customer Service team has no SOP for online transactions, there is a risk that complaints are not handled quickly or consistently, which may lead to customer dissatisfaction and issues spreading on social media.	Customer Service was not involved from the start of the project.	Complaint backlog, delayed refunds, and reputational damage.	Complaint SOP for in-store purchases only (does not cover online). **Ineffective**	Develop an online complaint SOP and escalation path (Customer Service → IT/Store Operations → Finance for refunds), prepare response templates, and brief the team. **Owner:** Customer Service Lead · **Due:** 7 Oct · **Status:** Open
R-09 **App slowdown or outage under high traffic** IT · IT **CRITICAL · 15**	Because the large campaign will drive many simultaneous visitors, there is a risk that the app becomes slow or inaccessible on launch day, which may result in lost first-day sales.	Server capacity has not been tested for traffic spikes.	Lost sales and wasted campaign spend.	Standard server monitoring. **Needs Improvement**	Run load tests simulating high user volumes on the core journey; provision additional server capacity; keep the IT team on standby during launch. **Owner:** IT Infrastructure Lead · **Due:** 8 Oct · **Status:** Open
R-10 **Order status notifications not delivered** IT · IT **MEDIUM · 9**	Because the notification system has not been tested together with the inventory and payment systems, there is a risk that customers do not receive notifications such as “order ready for pickup,” which may cause them to arrive too early or not at all.	Notifications depend on inventory and payment data that are not yet stable.	Uncollected orders pile up in pickup areas; repeat store visits; complaints.	None in place. **Ineffective**	Test notifications end to end across the order journey; provide order status checks in the app and through Customer Service. **Owner:** QA Lead · **Due:** 8 Oct · **Status:** Open
R-11 **Customer personal data breach** IT / Legal · Compliance **HIGH · 10**	Because the new app stores customers' personal data and transaction history, there is a risk that security vulnerabilities are exploited by external parties, which may result in a data breach and sanctions under Indonesia's Personal Data Protection Law (UU PDP).	Security testing has not been prioritized.	Fines, legal claims, and loss of customer trust.	Certified payment gateway (card data handled by the vendor). **Needs Improvement**	Conduct a basic security review before launch; restrict data access to teams that need it; display the privacy policy in the app. **Owner:** IT Security Lead · **Due:** 9 Oct · **Status:** Open
R-12 **Payment data mismatch across systems** Finance · Financial **MEDIUM · 9**	Because transactions now come from the app, the payment gateway, and store cashiers, there is a risk that payment data does not match across systems, which may cause recording discrepancies and delayed refunds.	No daily reconciliation process exists for online transactions.	Cash discrepancies, delayed financial reporting, and slow refunds.	Daily reconciliation for in-store cashiers. **Needs Improvement**	Establish a daily reconciliation process (app vs. payment gateway vs. stores) and assign a Finance owner for refunds. **Owner:** Finance Controller · **Due:** 9 Oct · **Status:** Open
R-13 **Additional costs exceed the budget** Finance / PMO · Financial **HIGH · 12**	Because unplanned needs have emerged (additional testers, overtime, logistics vendor fees), there is a risk that total costs exceed the approved budget, which may lead to rejection by Finance and delayed decisions.	Additional needs only became visible in the final stage of the project.	Conflict with Finance; work delayed while awaiting approval.	Monthly cost reports. **Needs Improvement**	Record all additional costs through change requests; fund them only from the contingency reserve; review costs weekly with Finance. **Owner:** Project Manager · **Due:** 6 Oct · **Status:** Open
R-14 **Stakeholder misalignment on launch scope** PMO / Stakeholders · Strategic **HIGH · 12**	Because the CEO, Marketing, Finance, and Store Operations have differing expectations, there is a risk that the Go/No-Go decision is delayed or keeps changing, which may leave the team without clear direction in the final week.	Launch success criteria were not agreed upon at the outset.	Rework; time spent on debate rather than fixes.	Weekly project meetings. **Needs Improvement**	Agree on written Go/No-Go criteria; schedule a decision meeting with the CEO as the final decision-maker. **Owner:** Project Manager · **Due:** 6 Oct · **Status:** Open
R-15 **Late feature requests before launch** PMO · Strategic **HIGH · 12**	Because Marketing wants all key features available, there is a risk of new feature or change requests in the final week, which may divide the team's focus and delay defect fixes.	No scope freeze rule is in place before launch.	Schedule slippage; lower deliverable quality.	Change request process not strictly enforced. **Ineffective**	Enforce a code freeze 3 days before launch; log all new requests for Phase 2. **Owner:** Project Manager · **Due:** 7 Oct · **Status:** Open

Risk	Risk description	Root cause	Business consequences	Existing controls	Mitigation actions
R-16 **Key team members unavailable** IT · Operational **MEDIUM · 8**	Because only a few developers understand the payment and inventory integrations, there is a risk that a key person becomes ill, resigns, or burns out before launch, which may halt defect fixing.	Technical knowledge is concentrated in 1–2 people; overtime hours are high.	Delayed fixes; risk of a failed launch.	None in place. **Ineffective**	Document critical configurations; pair each key developer with a backup; rotate overtime schedules. **Owner:** IT Lead · **Due:** 7 Oct · **Status:** Open
R-17 **Unclear in-store returns for online orders** Store Operations · Operational **MEDIUM · 9**	Because there are no rules for returning online orders in store, there is a risk that staff refuse or incorrectly process returns, which may cause customer dissatisfaction and stock discrepancies.	The returns SOP covers in-store purchases only.	Complaints, stock discrepancies, and financial discrepancies.	In-store returns SOP. **Needs Improvement**	Create interim return rules for online orders at pilot stores and include them in cashier training. **Owner:** Store Operations Lead · **Due:** 8 Oct · **Status:** Open
R-18 **Store devices not ready for pickup process** Store Operations / IT · Operational **MEDIUM · 9**	Because store staff need devices (scanners or tablets) to verify orders, there is a risk that devices are unavailable or not connected to the system, which may result in slow, error-prone manual verification.	Device requirements were not included in the procurement plan.	Long queues; items handed to the wrong customer.	None in place. **Ineffective**	Check device availability at pilot stores; prepare a fallback verification method using the order code and phone number. **Owner:** Store Operations Lead · **Due:** 8 Oct · **Status:** Open
R-19 **Slow vendor response to payment errors** IT / Vendor · IT **HIGH · 12**	Because fixing payment errors depends on the payment gateway vendor, there is a risk that the vendor cannot deliver fixes on time, which may make certain payment methods unavailable at launch.	The vendor contract does not include an SLA for fix turnaround.	Limited payment options; potential lost sales.	Standard vendor support contact. **Needs Improvement**	Escalate to the vendor's account manager; request a written fix schedule; prepare alternative payment methods. **Owner:** IT Lead · **Due:** 6 Oct · **Status:** Open
R-20 **No service owner after project closure** Operations / Business Owner · Strategic **HIGH · 12**	Because the team is currently focused on launch, there is a risk that no one has been assigned to manage the app, online inventory, and complaints after project closure, which may lower service quality and prevent business benefits from being realized.	No handover plan to the operations team has been prepared.	Unsustainable service: the project succeeds, but the business outcome fails.	None in place. **Ineffective**	Appoint a business owner (Head of Omnichannel); prepare a handover plan with a 2-week post-launch support period. **Owner:** Project Manager · **Due:** 24 Oct · **Status:** Open
R-21 **Stores overwhelmed by launch orders** Store Operations · Operational **MEDIUM · 9**	Because the grand launch promotion may attract a high volume of orders at once, there is a risk that pickup orders exceed staff and pickup area capacity, which may delay order preparation and cause long queues.	Order volume per store has not been forecast.	Customer complaints; staff fatigue.	None in place. **Ineffective**	Cap daily pickup orders per store during the first week; add staff shifts during launch. **Owner:** Store Operations Lead · **Due:** 9 Oct · **Status:** Open
R-22 **Unclear or non-compliant promotion terms** Marketing / Legal · Compliance **MEDIUM · 6**	Because the launch promotion was prepared in a short time, there is a risk that its terms and conditions are unclear or do not comply with consumer protection rules, which may lead to complaints and compensation obligations.	Promotion materials have not been reviewed by the legal team.	Complaints, customer compensation, and regulatory warnings.	None in place. **Ineffective**	Review the promotion terms with the legal team; display the terms and conditions clearly in the app. **Owner:** Marketing Lead · **Due:** 7 Oct · **Status:** Open
R-23 **App errors on certain phone models** IT / QA · IT **MEDIUM · 9**	Because testing has been performed on only a few device types, there is a risk that the app fails on certain phone models or operating system versions, which may prevent some customers from shopping.	Limited list of test devices.	Loss of some customers; negative app store reviews.	Testing on a few internal devices. **Needs Improvement**	Test on the Android and iOS devices most commonly used by customers; monitor crash reports after launch. **Owner:** QA Lead · **Due:** 8 Oct · **Status:** Open

Risk	Risk description	Root cause	Business consequences	Existing controls	Mitigation actions
R-24 **Low customer adoption of the app** Marketing / Business Owner · Strategic **MEDIUM · 9**	Because customers are accustomed to shopping in store, there is a risk of low app usage after launch, which may prevent online sales targets from being met.	No incentives or education on using the app.	Project benefits not realized as estimated.	Grand launch campaign. **Needs Improvement**	Offer a first-purchase promotion in the app; have store staff help customers install the app; track weekly active users. **Owner:** Marketing Lead · **Due:** 24 Oct · **Status:** Monitoring
R-25 **Phased launch details not reaching all stores** Store Operations · Operational **MEDIUM · 6**	Because the phased launch decision was made close to launch, there is a risk that staff at non-pilot stores are unaware of which services are available, which may result in customers receiving incorrect information.	No official project communication channel to all stores.	Customer confusion; complaints.	Area manager chat group. **Needs Improvement**	Send an official summary (FAQ) to all stores before launch; brief all area managers. **Owner:** Store Operations Lead · **Due:** 9 Oct · **Status:** Open

Notes

Scoring scale. Risk Score = Likelihood × Impact, each rated 1–5. Levels follow the template formula: 1–4 Low, 5–9 Medium, 10–14 High, 15–25 Critical.
Timeline assumption. Target completion dates are based on a planned launch of 10 October 2026, with the review conducted on 3 October 2026.
