• BOOTCAMP CASE STUDY · MINI PROJECT 4

OCTOBER 2026

SHOPEE LIVE INSTANT CHECKOUT

Project execution plan from schedule, cost, quality to risk

Jenna Gozali

Project Manager / Product Owner (case role)

Business Analyst & Product Strategy Bootcamp · dibimbing.id

Case study only, not affiliated with Shopee

TABLE OF CONTENTS

01 The problem

02 The solution

03 Objectives

04 Approach & governance

05 WBS & timeline in Jira

06 Team & budget

07 Quality & risk

08 Launch, evaluation & lessons

01 · THE PROBLEM

BUYERS LOSE THE RACE FOR STOCK

1.8%
checkout conversion rate on Shopee Live

70%
of buyers drop off on the payment page

51.1%
of simulated checkouts failed because stock ran out mid-payment

0%
conversion for Gen Z, who make up 54% of monthly users

A 7–9 tap checkout with no stock lock: the longer it takes, the more likely someone else buys the last unit. Estimated potential loss: ≈ Rp 45.5bn per month.

Source: my Mini Project 1 & 2 research (45 simulated checkouts, user interviews)

02 · THE SOLUTION

ONE MVP, FOUR BUILDING BLOCKS

Stock reservation

1 unit is held for 5 minutes the moment a buyer taps Buy Now, then released automatically if unpaid.

Checkout overlay

2–3 taps without leaving the live stream; address, voucher and courier prefilled but editable.

PIN confirmation

ShopeePay PIN before payment, locked after 3 wrong attempts, to stop accidental purchases.

2-minute grace period

Free cancellation right after paying; stock goes straight back to the live session.

Validated in Mini Project 3: the prototype checkout took 10 seconds and 3 taps, versus 98 seconds and 8 taps on the current flow.

Plus a real-time live stock indicator, KPI dashboard and a kill switch

03 · OBJECTIVES

WHAT SUCCESS LOOKS LIKE

Checkout conversion rate	1.8% → 5.4%	KPI dashboard, 4 weeks post-launch
Checkouts lost to stock running out	51.1% → <10%	Stock-loss failure rate
Steps to complete checkout	7–9 → 2–3 + PIN	Funnel event tracking
Refunds from accidental purchases	≤0.5% of orders	CS tickets & grace-period cancels
Delivery against the baseline	≤10% variance	Schedule & cost, actual vs plan

04 · APPROACH & GOVERNANCE

PHASE GATES OUTSIDE, KANBAN INSIDE

Six milestones give the sponsor clear go / no-go points, while the team runs day-to-day work on a Kanban board in Jira. A phase only starts after the previous milestone is approved.

TICKET WORKFLOW — NOTHING REACHES DONE WITHOUT QA



Daily rhythm
15-min stand-up, Friday status update to the sponsor

Sponsor decides
Scope changes, delays over 5 days, costs over 5% of budget

Change control
New requests go through a change request, not straight into the sprint

05 · WORK BREAKDOWN IN JIRA


EPIC › STORY / TASK › SUBTASK

7
epics, one per phase

30
stories & tasks with dates

85
subtasks with an assignee

36
finish-to-start dependencies

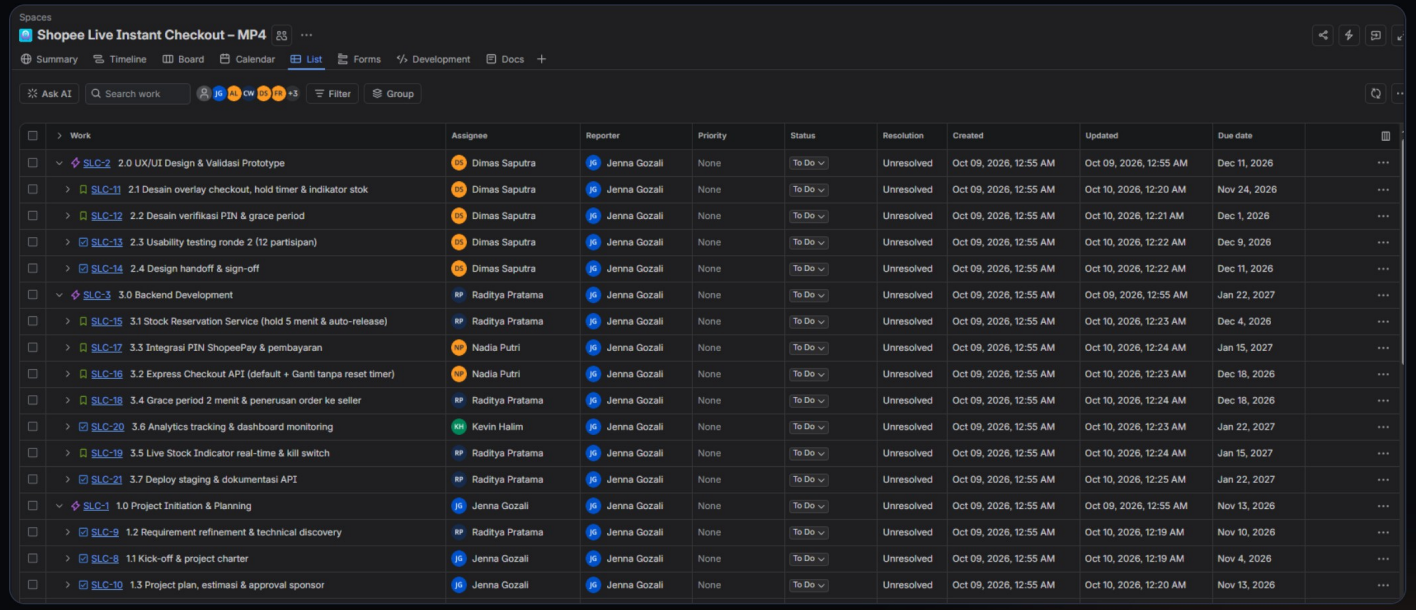


Work	Assignee	Reporter	Priority	Status	Resolution	Created	Updated	Due date
SLC-2 2.0 UX/UI Design & Validasi Prototype	Dimas Saputra	Jenna Gozali	None	To Do	Unresolved	Oct 09, 2026, 12:55 AM	Oct 09, 2026, 12:55 AM	Dec 11, 2026
SLC-11 2.1 Desain overlay checkout, hold timer & indikator stok	Dimas Saputra	Jenna Gozali	None	To Do	Unresolved	Oct 09, 2026, 12:55 AM	Oct 10, 2026, 12:20 AM	Nov 24, 2026
SLC-12 2.2 Desain verifikasi PIN & grace period	Dimas Saputra	Jenna Gozali	None	To Do	Unresolved	Oct 09, 2026, 12:55 AM	Oct 10, 2026, 12:21 AM	Dec 1, 2026
SLC-13 2.3 Usability testing ronde 2 (12 partisipan)	Dimas Saputra	Jenna Gozali	None	To Do	Unresolved	Oct 09, 2026, 12:55 AM	Oct 10, 2026, 12:22 AM	Dec 9, 2026
SLC-14 2.4 Design handoff & sign-off	Dimas Saputra	Jenna Gozali	None	To Do	Unresolved	Oct 09, 2026, 12:55 AM	Oct 10, 2026, 12:22 AM	Dec 11, 2026
SLC-3 3.0 Backend Development	Raditya Pratama	Jenna Gozali	None	To Do	Unresolved	Oct 09, 2026, 12:55 AM	Oct 09, 2026, 12:55 AM	Jan 22, 2027
SLC-15 3.1 Stock Reservation Service (hold 5 menit & auto-release)	Raditya Pratama	Jenna Gozali	None	To Do	Unresolved	Oct 09, 2026, 12:55 AM	Oct 10, 2026, 12:23 AM	Dec 4, 2026
SLC-17 3.3 Integrasi PIN ShopeePay & pembayaran	Nadia Putri	Jenna Gozali	None	To Do	Unresolved	Oct 09, 2026, 12:55 AM	Oct 10, 2026, 12:24 AM	Jan 15, 2027
SLC-16 3.2 Express Checkout API (default + Ganti tanpa reset timer)	Nadia Putri	Jenna Gozali	None	To Do	Unresolved	Oct 09, 2026, 12:55 AM	Oct 10, 2026, 12:23 AM	Dec 18, 2026
SLC-18 3.4 Grace period 2 menit & penerusan order ke seller	Raditya Pratama	Jenna Gozali	None	To Do	Unresolved	Oct 09, 2026, 12:55 AM	Oct 10, 2026, 12:24 AM	Dec 18, 2026
SLC-20 3.6 Analytics tracking & dashboard monitoring	Kevin Halim	Jenna Gozali	None	To Do	Unresolved	Oct 09, 2026, 12:55 AM	Oct 10, 2026, 12:23 AM	Jan 22, 2027
SLC-19 3.5 Live Stock Indicator real-time & kill switch	Raditya Pratama	Jenna Gozali	None	To Do	Unresolved	Oct 09, 2026, 12:55 AM	Oct 10, 2026, 12:24 AM	Jan 15, 2027
SLC-21 3.7 Deploy staging & dokumentasi API	Raditya Pratama	Jenna Gozali	None	To Do	Unresolved	Oct 09, 2026, 12:55 AM	Oct 10, 2026, 12:25 AM	Jan 22, 2027
SLC-1 1.0 Project Initiation & Planning	Jenna Gozali	Jenna Gozali	None	To Do	Unresolved	Oct 09, 2026, 12:55 AM	Oct 09, 2026, 12:55 AM	Nov 13, 2026
SLC-9 1.2 Requirement refinement & technical discovery	Raditya Pratama	Jenna Gozali	None	To Do	Unresolved	Oct 09, 2026, 12:55 AM	Oct 10, 2026, 12:19 AM	Nov 10, 2026
SLC-8 1.1 Kick-off & project charter	Jenna Gozali	Jenna Gozali	None	To Do	Unresolved	Oct 09, 2026, 12:55 AM	Oct 10, 2026, 12:19 AM	Nov 4, 2026
SLC-10 1.3 Project plan, estimasi & approval sponsor	Jenna Gozali	Jenna Gozali	None	To Do	Unresolved	Oct 09, 2026, 12:55 AM	Oct 10, 2026, 12:20 AM	Nov 13, 2026

Jira List view: every ticket starts with its WBS number so it maps 1:1 to the plan document

Stories for buyer-facing work (user story format), tasks for testing, deployment and evaluation

05 · SCHEDULE BASELINE

23 WEEKS, SIX MILESTONES

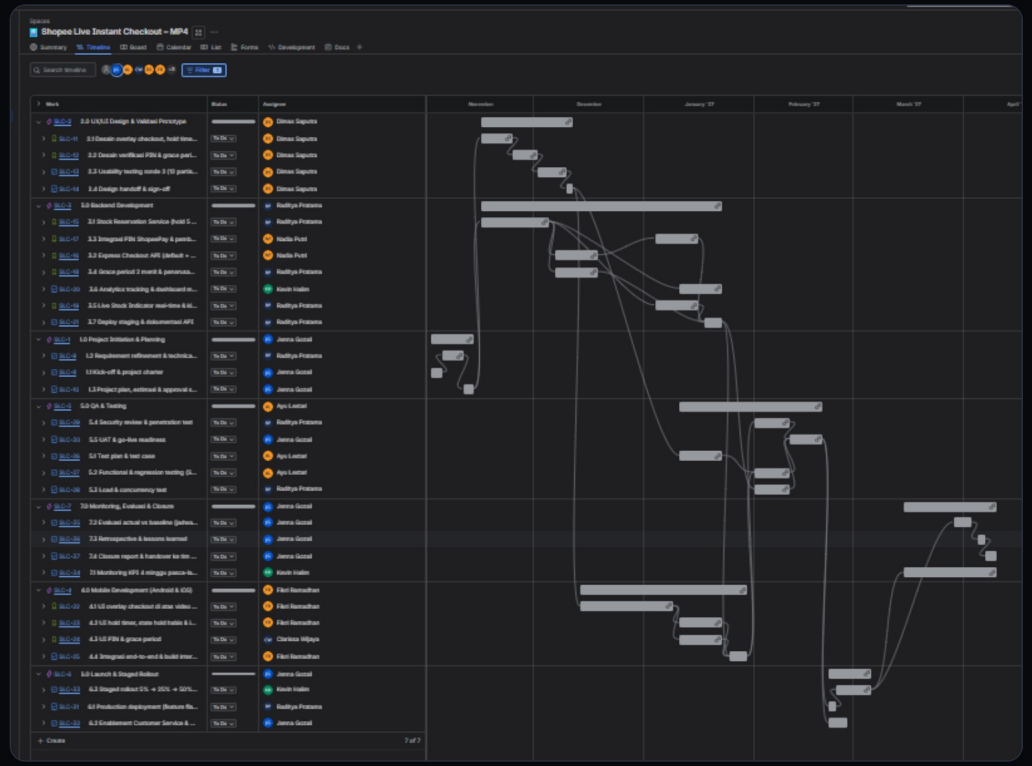

13 Nov 2026	M1 · Project plan approved
11 Dec 2026	M2 · Design sign-off after usability test (12 users)
29 Jan 2027	M3 · Development complete on staging
19 Feb 2027	M4 · UAT sign-off & go-live approval
5 Mar 2027	M5 · Rolled out to 100% of users
9 Apr 2027	M6 · Evaluation & project closure

Critical path: design → mobile build → testing → rollout. 11.11 / 12.12 code freezes, year-end and Lebaran holidays are built into the dates.

06 · TEAM & RESOURCES

EIGHT PEOPLE, 292 PERSON-DAYS

47 PD
Project Manager / PO
Jenna Gozali

53 PD
Backend Tech Lead
Stock reservation, load test

47 PD
Backend Engineer
Checkout API, PIN & payment

34 PD
Android Engineer
Overlay, integration

34 PD
iOS Engineer
PIN & grace period UI

20 PD
Product Designer
Final design, usability test

26 PD
QA Engineer
SIT, regression, UAT

30 PD
Data Analyst
Tracking, KPI dashboard

Bottom-up from each Jira subtask, levelled so nobody is booked above 100% on any day.

PD = person-days. Team members other than me are illustrative roles for the case study.

06 · COST BASELINE

BUDGETED BOTTOM-UP FROM JIRA


Rp 569.8M

Total budget, under the Rp 600M cap



- Team (8 people) · Rp 328.8M · 58%
- Pentest vendor, tools, cloud, incentives · Rp 142.1M · 25%
- Overhead 10% · Rp 47.1M · 8%
- Contingency reserve 10% · Rp 51.8M · 9%

Direct cost by phase (Rp M)

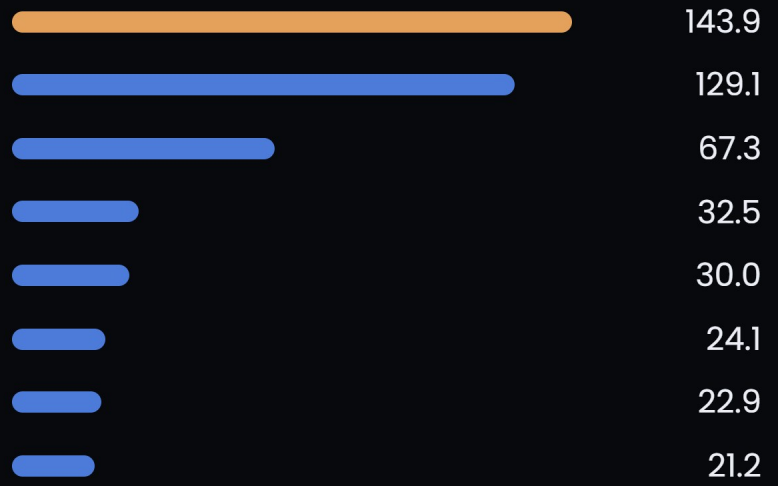

QA is the biggest phase on purpose: the feature touches money and stock in real time, so the pentest and load testing stay in.

Effort per subtask × daily rate per role, plus non-labour cost per activity. ≈1.3% of one month's estimated loss.

07 · QUALITY MANAGEMENT

NO RELEASE WHILE ANY GATE IS RED

0
oversold units in load test or production

≤200 ms
p95 reservation API at 3× peak traffic

0
open Critical / High bugs or pentest findings at go-live

≥99.8%
crash-free sessions on the new app version

≥80%
unit test coverage on reservation & payment code

≤35 s
median checkout time, PIN included

Quality assurance (process)

Design reviews with engineers, 2-person code review, Definition of Done, mandatory In Testing status


Quality control (product)

SIT on Android & iOS, load test at 3× peak, external pentest, UAT with seller reps

Full plan: 5W1H quality guide, 14-point feature checklist, metrics per process, weekly QA reporting

07 · RISK ANALYSIS

15 RISKS, SCORED AND MAPPED

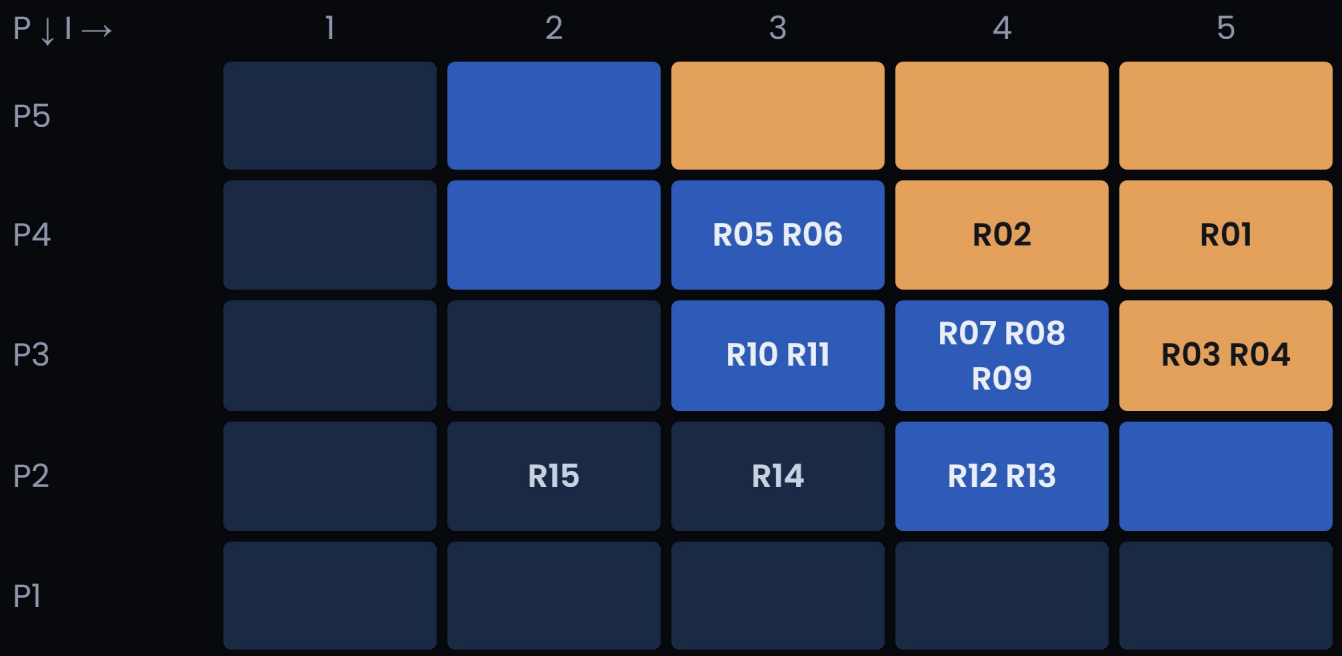

- High risk · score 15–25
- Medium risk · score 8–14
- Low risk · score 1–7

Score = probability × impact (1–5 each). Four categories: project (3), technical (4), resource (2) and other - business, security, compliance, adoption, cost (6).

Every risk has an owner and a response; High risks are also tracked as "Risk" tickets in Jira

07 · RISK RESPONSE

HOW THE TOP FOUR ARE HANDLED

R01 · Score 20 · High

Traffic spike takes the reservation service down

Mitigate

Load test at 3× peak, autoscaling and rate limits. Kill switch sends buyers back to the regular checkout.

R02 · Score 16 · High

Users or bots hoard stock with holds

Avoid + mitigate

One active hold per user per item, three per account, bot detection. Shorter hold if release rate passes 40%.

R03 · Score 15 · High

Two buyers both get the last unit

Avoid

Atomic reserve operations, last-unit concurrency tests and stock reconciliation every 5 minutes.

R04 · Score 15 · High

Paid, but no order — or charged twice

Mitigate + transfer

Idempotency keys, a reconciliation job and an agreed callback SLA with the payments team.

Backed by a Rp 51.8M contingency reserve, released only for risks on the log and only with sponsor approval.

Strategies used across the log: avoid, mitigate, transfer, accept

08 · LAUNCH & EVALUATION

ROLL OUT IN STEPS, THEN MEASURE

5%	→	25%	→	50%	→	100%
Gen Z, Jakarta · 24 Feb		26 Feb		3 Mar		5 Mar 2027

Each step only goes up if the guardrails hold: error rate under 0.5%, zero oversell, accidental-purchase refunds at or below 0.5%, and no more than 30% of holds released unpaid.

Actual vs baseline
Schedule and cost index (SPI, CPI) at 0.9 or better

KPI review
4 weeks of conversion, stock loss and refund data

Stakeholder survey
Sponsor, payments, CS and sellers, target 4 / 5

Retrospective
Start / stop / continue, feeding the next phase

Feature flag and kill switch let the team step back without shipping a new app version

08 · WHAT I LEARNED

LESSONS FROM PLANNING IT END TO END

01 Put campaign dates and holidays in before estimating. 11.11, 12.12 and Lebaran only showed their impact once the dates were in Jira.

02 Check allocation per person per day, not per epic. My first draft overbooked the designer and tech lead on review days.

03 For features that touch money, security and performance testing are about a quarter of the budget. Easy to miss if you only count salaries.

04 Validate with real sample sizes. Two test users pointed the way; the plan budgets 12 before release.

Skills I practised

Jira · WBS · Critical path · Resource levelling · Bottom-up costing · Quality management · Risk heat map · Stakeholder mapping · KPI & guardrails · Agile / Kanban · Staged rollout

• JENNA GOZALI

LET'S CONNECT

From user research to an execution plan: four mini projects on one product problem, Shopee Live checkout.

LinkedIn
www.linkedin.com/in/jennagozali
